




ID	Task Name	Duration	w.t	Cost	Baseline Start	Baseline Finish	duration.	Start	Finish	Duration	درصد پیشرفت	2024, Half 1												2024, Half 2					2025, Half 1					2025, Half 2					
												D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S						
1	تامین ۹۰ تن پلی الکترولیت کاتیونی-شماره قرارداد ۵۲۳۵۹/۲۱۲۰۶ آب جنوب تهران	437 days	100	ریال ۲۰۹,۸۸۰,۰۰۰,۰۰۰	Fri 24/03/03	Sat 24/09/02	312 days	Sun 24/03/03	Tue 25/05/13	436 days	88																												
2	شروع 1.1	1 day	0	ریال ۰	Fri 24/03/03	Fri 24/03/03	0 days	Sun 24/03/03	Sun 24/03/03	0 days	0	1402/12/13 1402/12/13 1402/12/13																											
3	اقدامات اولیه 1.2	281 days	20	ریال ۰	Fri 24/03/03	Fri 24/06/30	248 days	Sun 24/03/03	Sun 24/12/08	281 days	19	1402/12/13 1402/12/13 1402/12/14 1403/5/16																											
4	ابلاغ قرارداد 1.2.1	1 day	0	ریال ۰	Fri 24/03/03	Fri 24/03/03	1 day	Sun 24/03/03	Sun 24/03/03	1 day	0	1403/5/17 1403/5/17 1403/5/18 1403/5/18																											
5	اخذ تاییدیه ثبت سفارش از وزارت صمت	156 days	0	ریال ۰	Sat 24/03/11	Thu 24/05/18	156 days	Mon 24/03/04	Tue 24/08/06	156 days	0	1403/5/19 1403/8/4 1403/8/5 1403/8/10																											
6	ثبت سفارش 1.2.3	1 day	1	ریال ۰	Fri 24/05/19	Fri 24/05/19	1 day	Wed 24/08/07	Wed 24/08/07	1 day	0	1403/8/11 1403/9/18 1403/9/19 1403/9/19 1403/9/20 1403/11/9																											
7	تشریفات اداری و بانکی 1.2.4	1 day	3	ریال ۰	Sat 24/05/20	Sat 24/05/20	1 day	Thu 24/08/08	Thu 24/08/08	1 day	3	1403/11/10 1403/12/25 1403/12/26 1404/2/23																											
8	تخصیص ارز اولیه 1.2.5	78 days	6	ریال ۰	Sun 24/05/21	Mon 24/06/19	78 days	Fri 24/08/09	Fri 24/10/25	78 days	6	1403/12/26 1404/2/20																											
9	تخصیص ارز با توجه به تغییر ضوابط و تغییر گروه کالایی 1.2.6	6 days	1	ریال ۰	Tue 24/06/20	Sun 24/06/25	6 days	Sat 24/10/26	Thu 24/10/31	6 days	1	1403/2/22 1403/2/24 1404/2/23 1404/2/23																											
10	تامین و حواله ارز 1.2.7	38 days	9	ریال ۰	Mon 24/06/26	Fri 24/06/30	5 days	Fri 24/11/01	Sun 24/12/08	38 days	9																												
11	تامین و تدارک کالا 1.3	51 days	20	ریال ۱۹۹,۱۸۰,۰۰۰,۰۰۰	Sat 24/07/01	Fri 24/07/21	21 days	Mon 24/12/09	Tue 25/01/28	51 days	20																												
12	سفارش تولید کالا 1.3.1	1 day	1	ریال ۰	Sat 24/07/01	Sat 24/07/01	1 day	Mon 24/12/09	Mon 24/12/09	1 day	1																												
13	تولید کالا 1.3.2	50 days	19	ریال ۱۹۹,۱۸۰,۰۰۰,۰۰۰	Sun 24/07/02	Fri 24/07/21	20 days	Tue 24/12/10	Tue 25/01/28	50 days	19																												
14	حمل 1.4	45.38 days	50	ریال ۶,۵۰۰,۰۰۰,۰۰۰	Sat 24/07/22	Sun 24/08/20	30 days	Wed 25/01/29	Sat 25/03/15	45 days	49																												
15	حمل کالا به ایران 1.4.1	46 days	50	ریال ۶,۵۰۰,۰۰۰,۰۰۰	Sat 24/07/22	Sun 24/08/20	30 days	Wed 25/01/29	Sat 25/03/15	45 days	49																												
16	ترخیص و تحویل کالا 1.5	59.38 days	10	ریال ۴,۲۰۰,۰۰۰,۰۰۰	Mon 24/08/21	Sat 24/09/02	13 days	Sun 25/03/16	Tue 25/05/13	59 days	0																												
17	ترخیص گمرک 1.5.1	56 days	8	ریال ۲,۶۰۰,۰۰۰,۰۰۰	Mon 24/08/21	Wed 24/08/30	10 days	Sun 25/03/16	Sat 25/05/10	56 days	0																												
18	تحویل کالا 1.5.2	3 days	2	ریال ۱,۶۰۰,۰۰۰,۰۰۰	Thu 24/08/31	Sat 24/09/02	3 days	Sat 24/05/11	Mon 24/05/13	3 days	0																												
19	پایان 1.5.3	1 day	0	ریال ۰	Sat 24/09/02	Sat 24/09/02	0 days	Tue 25/05/13	Tue 25/05/13	0 days	0																												

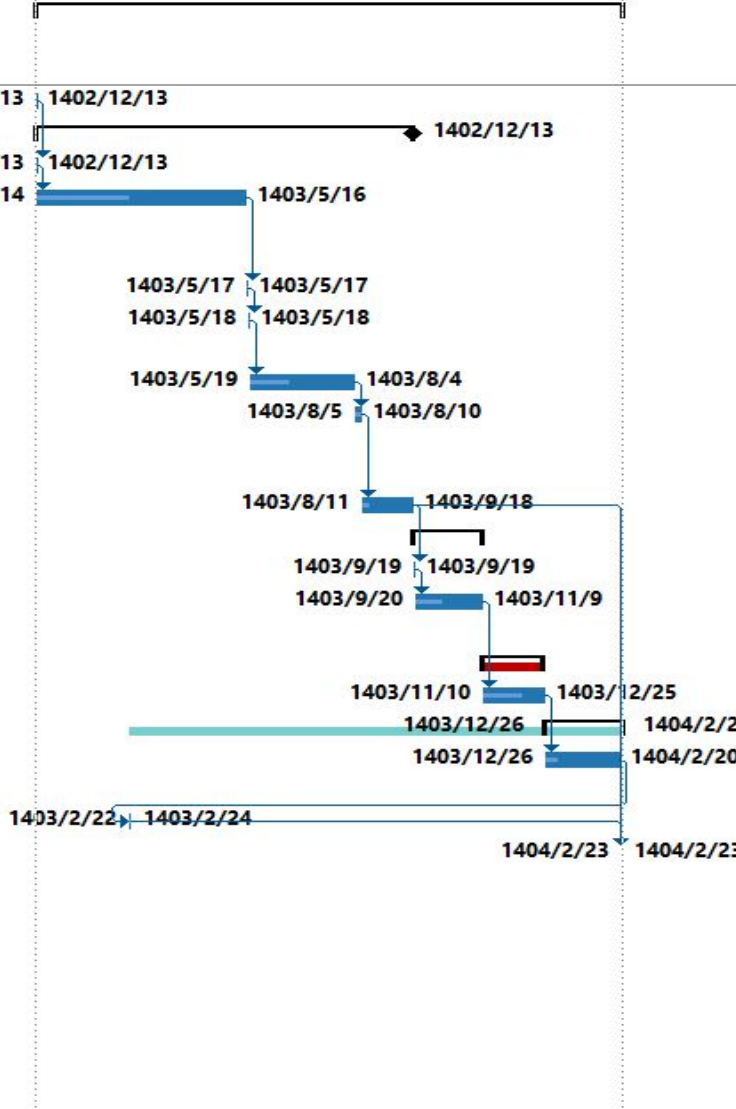

Project: Project1
Date: Wed 25/12/17

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Path Driven Successor Milestone Task

Path Driven Successor Summary Task

Path Driven Successor Normal Task

Baseline

Baseline Milestone

Baseline Summary

Progress

Manual Progress
